


Shop Drawings

WORK ORDER WORKSHOP REPORT - 11/Mar/2025 01:21 PM Chris.Mills10@det.nsw.edu.au				
W/O Number:	WS18112024-1	Job Number:	22745	
Date Issued:	11/Mar/2025 01:21 PM	Date Required:	14/Sep/2024 12:00 AM	
W/O Raised By:	Chris Mills	Client:	NSW010 - NSW Department of Education	
Job Location:	EDCONNECT - ACCOUNTS PAYABLE GPO BOX 4037 SYDNEY NSW		EDCONNECT - ACCOUNTS PAYABLE GPO BOX 4037 SYDNEY NSW	

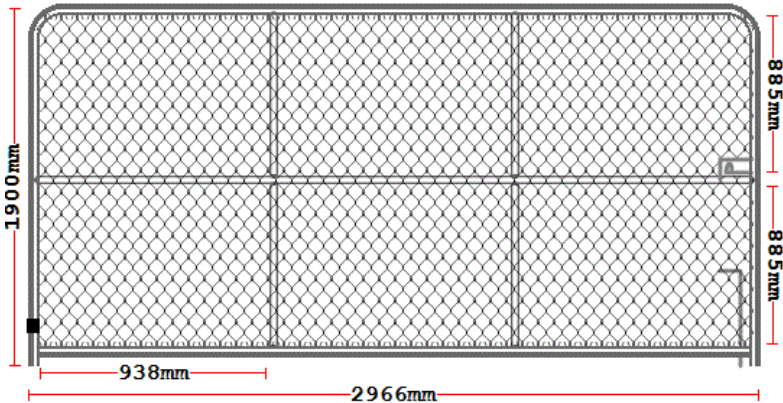

NOMINAL WIDTH	3000
NOMINAL HEIGHT	1800
CHAIN LINK	50x3.15 KK Heavy Galvanized
SELECTED CHAIN LINK FABRIC HEIGHT	[22 LESS 0.5 DIAMOND] 1804
ACTUAL FRAME HEIGHT	1900
*GATE FRAME GALVANIZED FINISH	

ITEM	TIME	RATE	QTY	TOTAL
Stage 1, Cutting, Notching	28.75	90	0.48	43.12
Stage 2.A & 2.B Welding	83.5	90	1.39	125.25
Stage 3. Lacing Chain Link to Gates	75.12	90	1.25	112.68
Set Up Time Between 3 Stages @ 6.0 min	18	90	0.30	27

403 Forbidden
